Mersey Gateway
Indicative Construction Programme

Original Size A3

ID	Task Name	Duration	Start	Finish	Bar Comments
1	**Mersey Gateway**	**202.2 wks**	**01/01/00**	**17/11/03**	
2	Financial Close	0 days	01/01/00	01/01/00	nancial Close
3	General Mobilisation	26 wks	03/01/00	30/06/00	
4	Design Period	26 wks	03/01/00	30/06/00	
5					
6	Mersey Gateway Opens	1 day	21/04/03	21/04/03	ns to Opening
7	**WIDNES**	**146.2 wks**	**30/06/00**	**21/04/03**	
8	**Area A**	**123.2 wks**	**03/07/00**	**11/11/02**	
9	Site Clearance	13 wks	03/07/00	29/09/00	
10	Ground Improvement	5 wks	02/10/00	03/11/00	
11	Southbound Off-slip from Speke Road	13 wks	29/01/01	27/04/01	
12	Northbound On-slip to Speke Road	9 wks	30/04/01	29/06/01	
13	Mainline West of Ditton	13 wks	13/08/02	11/11/02	
14	**Area B1 Ditton Junction**	**146.2 wks**	**03/07/00**	**21/04/03**	
15	Ditton Road Approach widening	13 wks	03/07/00	29/09/00	
16	Ashley Way / Moor Lane Junction	17 wks	02/10/00	26/01/01	
17	Construct Ditton Bridge	26 wks	31/12/01	28/06/02	
18	Highway & Signals within Roundabout	13 wks	01/07/02	27/09/02	
19	Demolish 2 No Existing Bridges (ALAP)	9 wks	19/11/02	20/01/03	
20	Approach embankments	13 wks	21/01/03	21/04/03	
21	**Traffic Management**	**68.2 wks**	**31/12/01**	**21/04/03**	
22	**Phase 1**	**26 wks**	**31/12/01**	**28/06/02**	
25	**Phase 2**	**13 wks**	**01/07/02**	**27/09/02**	
28	**Phase 3 (Bridge Open)**	**29.2 wks**	**27/09/02**	**21/04/03**	
31	**Area B2: Ditton to Freight Line**	**133.2 wks**	**02/10/00**	**21/04/03**	
32	Site Clearance	13 wks	02/10/00	29/12/00	
33	Ground Improvement	26 wks	28/05/01	23/11/01	
34	Ditton On-slip	9 wks	10/09/02	11/11/02	
35	Mainline	10 wks	12/11/02	20/01/03	
36	Ditton Off-slip	9 wks	18/02/03	21/04/03	
37	Freight Line Bridge	26 wks	01/01/01	29/06/01	
38	**Area C Freight Line to St Helens Canal**	**146.2 wks**	**30/06/00**	**21/04/03**	
39	Site Clearance	39 ewks	30/06/00	30/03/01	
40	Ground Improvement	30 wks	30/10/00	25/05/01	
41	Canal Bridge / Widnes Abutment	25 wks	08/01/01	29/06/01	
42	Mainline East Bridge	20 wks	19/03/01	03/08/01	
43	Mainline West Bridge	20 wks	28/05/01	12/10/01	
44	Victoria Road Bridge	26 ewks	29/06/01	28/12/01	
45	Roundabout	13 wks	06/08/01	02/11/01	
46	Widnes eastern Bypass	13 wks	24/12/01	22/03/02	
47	Southbound On-slip	9 wks	21/01/02	22/03/02	
48	Excavate Embankments (ALAP)	9 wks	30/07/02	30/09/02	
49	Demolish Eastern Bypas bridges	6 wks	01/10/02	11/11/02	
50	Northbound Off-slip	9 wks	01/10/02	02/12/02	
51	Mainline Freightline to Victoria	10 wks	03/12/02	10/02/03	
52	Mianline Loops to Canal	10 wks	11/02/03	21/04/03	
53	**Traffic Management**	**94.2 wks**	**29/06/01**	**21/04/03**	
54	**Phase 1 (Two-way on northbound)**	**56.2 wks**	**29/06/01**	**30/07/02**	
57	**Phase 2 (Full diversion)**	**38 wks**	**30/07/02**	**21/04/03**	
60	**RIVER CROSSING**	**146 wks**	**03/07/00**	**18/04/03**	
61	**Offsite**	**104 wks**	**03/07/00**	**28/06/02**	
62	Setup Casting Area	26 wks	03/07/00	29/12/00	
63	Unit Storage Areas	13 wks	02/10/00	29/12/00	
64	Batching Plants	8 wks	06/11/00	29/12/00	
65	Hover Platforms	39 wks	03/07/00	30/03/01	
66	Unit production	78 wks	01/01/01	28/06/02	
67	Unit Delivery	56 wks	02/04/01	26/04/02	
68					
69	North Abutment	25 wks	03/07/00	22/12/00	
70	**D1 North Approach**	**133 wks**	**02/10/00**	**18/04/03**	
71	Access	12 wks	02/10/00	22/12/00	
72	Piers	26 ewks	28/09/01	29/03/02	
73	Gantry Setup West	4 wks	25/03/02	19/04/02	
74	West Deck	20 wks	22/04/02	06/09/02	
75	Gantry Setup East	4 wks	09/09/02	04/10/02	
76	East Deck	20 wks	07/10/02	21/02/03	
77	Wings	17 wks	23/12/02	18/04/03	
78	**D2 Main Bridge**	**124 wks**	**03/07/00**	**15/11/02**	
79	Jetty	17 wks	03/07/00	27/10/00	
80	Tower 1	52 wks	30/10/00	26/10/01	
81	Tower 2	52 wks	25/12/00	21/12/01	
82	Tower 3	52 wks	19/02/01	15/02/02	
83	Deck 1	39 wks	29/10/01	26/07/02	
84	Deck 2	39 wks	24/12/01	20/09/02	
85	Deck 3	39 wks	18/02/02	15/11/02	
86	**D3 Southern Approach**	**107 wks**	**03/07/00**	**19/07/02**	
87	Access	13 wks	03/07/00	29/09/00	
88	Piers	52 wks	02/10/00	28/09/01	
89	Gantry Setup West	12 wks	26/02/01	18/05/01	
90	West Deck	20 wks	21/05/01	05/10/01	
91	Gantry Setup East	4 wks	08/10/01	02/11/01	
92	East Deck	20 wks	05/11/01	22/03/02	
93	Wings	17 wks	25/03/02	19/07/02	
94	South Abutment	39 wks	14/08/00	11/05/01	
95	Carriageway Works	17 wks	23/12/02	18/04/03	
96	Deck Finishes	26 wks	21/10/02	18/04/03	
97	**RUNCORN**	**176.2 wks**	**03/07/00**	**17/11/03**	
98	**AREA E Astmoor Viaduct**	**83 wks**	**03/07/00**	**01/02/02**	
99	Site Clearance	17 wks	03/07/00	27/10/00	
100	South Abutments	35 wks	14/05/01	11/01/02	
101	Piers	39 wks	14/08/00	11/05/01	
102	Decks	52 ewks	03/11/00	02/11/01	
103	Carriageway	13 wks	05/11/01	01/02/02	
104	**Area F Bridgewater Junction**	**104 wks**	**03/07/00**	**28/06/02**	
105	Canal Bridges	39 wks	03/07/00	30/03/01	
106	South Flyover Abutment	13 wks	03/07/00	29/09/00	
107	North Flyover Abutment	13 wks	02/04/01	29/06/01	
108	Demolish Existing Road Bridges	13 wks	02/07/01	28/09/01	
109	Piers	13 wks	02/07/01	28/09/01	
110	Fly-over Deck	26 wks	01/10/01	29/03/02	
111	Demolish Canal Bridges	13 wks	01/04/02	28/06/02	
112	Remove Redundant Carriageway	13 wks	01/04/02	28/06/02	
113	Northbound Off-slip	13 wks	02/10/00	29/12/00	
114	Southbound On-slip	13 wks	02/10/00	29/12/00	
115	Daresbury Expressway	13 wks	28/01/02	26/04/02	

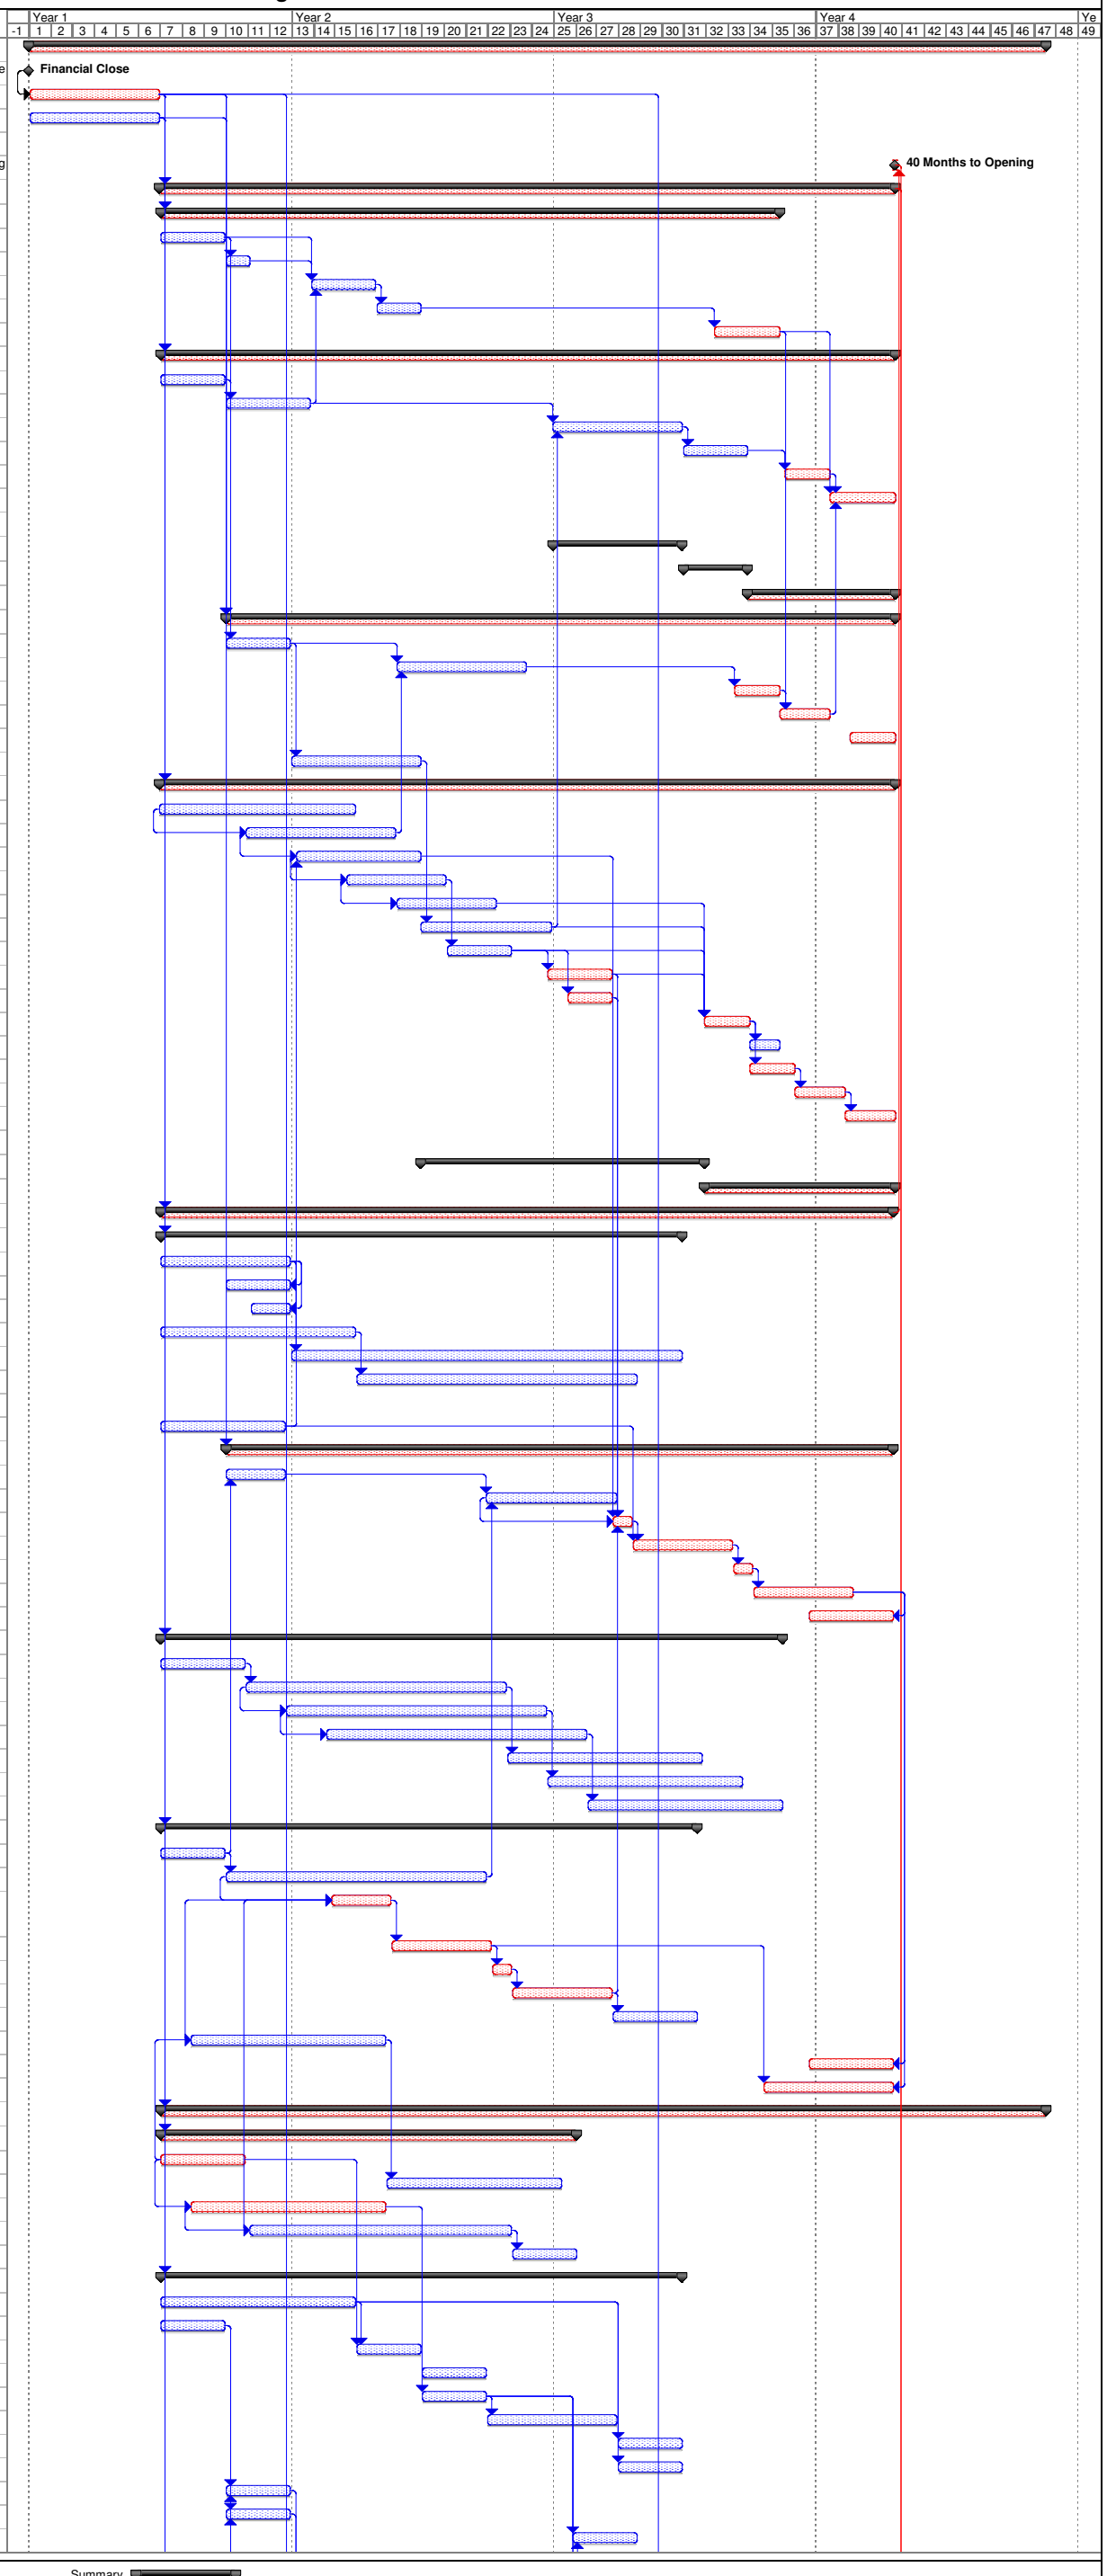

Project: Construction Prog 20111112_
Date: 14/11/11

Task Task Milestone Summary

Mersey Gateway
Indicative Construction Programme

Original Size A3

ID	Task Name	Duration	Start	Finish	Bar Comments
116	Bridgewater Expressway	13 wks	28/01/02	26/04/02	
117	Roundabout	13 wks	28/01/02	26/04/02	
118	**Traffic Management**	**104 wks**	**03/07/00**	**28/06/02**	
119	**Phase 1**	**39 wks**	**03/07/00**	**30/03/01**	
122	**Phase 2**	**13 wks**	**30/03/01**	**29/06/01**	
125	**Phase 3**	**39 wks**	**29/06/01**	**29/03/02**	
128	**Phase 4**	**13 wks**	**29/03/02**	**28/06/02**	
131	**AREA G1 Bridgewater to Halton Brow**	**31 wks**	**01/01/01**	**03/08/01**	
132	Northbound Slip from Halton Brow	13 wks	01/01/01	30/03/01	
133	Northbound Diverge	9 wks	02/04/01	01/06/01	
134	Southbound Merge	13 wks	01/01/01	30/03/01	
135	Southbound Off-slip to Halton Brow	9 wks	02/04/01	01/06/01	
136	Central Reserve	9 wks	04/06/01	03/08/01	
137	**AREA G2 Halton Brow to Halton Lea**	**95 wks**	**03/07/00**	**26/04/02**	
138	Southbound Reatining Wall	10 wks	03/07/00	08/09/00	
139	Northbound (ID4 Living) Wall	10 wks	11/09/00	17/11/00	
140	Widening for traffic signal	9 wks	11/09/00	10/11/00	
141	Southbound Distributor / Offslip	17 wks	04/06/01	28/09/01	
142	Northbound Distributor / Onslip	17 wks	01/10/01	25/01/02	
143	Works to Central Reserve	9 wks	28/01/02	29/03/02	
144	Resurface Southbound	2 wks	01/04/02	12/04/02	
145	Resurface Northbound	2 wks	15/04/02	26/04/02	
146	**AREA G3 Halton Lea Junction**	**13 wks**	**03/07/00**	**29/09/00**	
147	Roundabout Improvements	13 wks	03/07/00	29/09/00	
148	**AREA G4 Lodge Lane**	**52 wks**	**04/06/01**	**31/05/02**	
149	**Lodge Lane Bridge**	**39 wks**	**04/06/01**	**01/03/02**	
150	East Abutment (ALAP)	13 wks	04/06/01	31/08/01	
151	West Abutment	13 wks	03/09/01	30/11/01	
152	Deck	13 wks	03/12/01	01/03/02	
153	Southbound Offline Earthworks	26 wks	04/06/01	30/11/01	
154	Southern to Weston Point Link	9 wks	04/06/01	03/08/01	
155	Footbridge	3 mons	04/06/01	24/08/01	
156	Southern to Central	8 wks	04/03/02	26/04/02	
157	Central to Southern	8 wks	04/03/02	26/04/02	
158	Bridge Approaches / Mainline	13 wks	03/12/01	01/03/02	
159	Weston to Central	13 wks	04/03/02	31/05/02	
160	**Traffic Management**	**52 wks**	**04/06/01**	**31/05/02**	
161	**Phase 1**	**13 wks**	**04/06/01**	**31/08/01**	
164	**Phase 2**	**26 wks**	**31/08/01**	**01/03/02**	
167	**Phase 3**	**13 wks**	**01/03/02**	**31/05/02**	
170	**AREA G5 Weston Link Junction**	**30 wks**	**03/06/02**	**27/12/02**	
171	Equestrian Bridge	10 wks	05/08/02	11/10/02	
172	Northbound Link Improvement	8 wks	04/11/02	27/12/02	
173	Southbound Link Realignment	9 wks	03/06/02	02/08/02	
174	Weston Point Xway to Link	13 wks	05/08/02	01/11/02	
175	Demolish Part Structure	4 wks	04/11/02	29/11/02	
176	Remove Redundant Carriageway	2 wks	04/11/02	15/11/02	
177	**Traffic Management**	**30 wks**	**03/06/02**	**27/12/02**	
178	**Phase 1**	**9 wks**	**03/06/02**	**02/08/02**	
181	**Phase 2**	**13 wks**	**02/08/02**	**01/11/02**	
184	**Phase 3**	**8 wks**	**01/11/02**	**27/12/02**	
187	**AREA H M56 J12**	**54 wks**	**03/07/00**	**13/07/01**	
188	Site Clearance	8 wks	03/07/00	25/08/00	
189	Retaining Wall	26 wks	28/08/00	23/02/01	
190	Widen Realign Approaches	13 wks	23/10/00	19/01/01	
191	Infill Weston Point and M56 Link Approaches	9 wks	22/01/01	23/03/01	
192	Infill Roundabout	10 wks	26/03/01	01/06/01	
193	Traffic Signals	6 wks	04/06/01	13/07/01	
194	**Traffic Management**	**46 wks**	**28/08/00**	**13/07/01**	
195	**Phase 1**	**26 wks**	**28/08/00**	**23/02/01**	
198	**Phase 2**	**4 wks**	**23/02/01**	**23/03/01**	
201	**Phase 3**	**16 wks**	**23/03/01**	**13/07/01**	
204	**AREA I SILVER JUBILEE BRIDGE**	**30 wks**	**22/04/03**	**17/11/03**	
205	West Bank Links	13 wks	22/04/03	21/07/03	
206	West Bank Tolling	13 wks	20/05/03	18/08/03	
207	Queensway Links	17 wks	22/07/03	17/11/03	
208	SJB modifications	17 wks	22/04/03	18/08/03	
209	**Traffic Management**	**30 wks**	**22/04/03**	**17/11/03**	
210	**Phase 1**	**17 wks**	**22/04/03**	**18/08/03**	
211	Start	0 days	22/04/03	22/04/03	
212	End	0 days	18/08/03	18/08/03	
213	**Phase 2**	**13 wks**	**18/08/03**	**17/11/03**	
214	Start	0 days	18/08/03	18/08/03	
215	End	0 days	17/11/03	17/11/03	

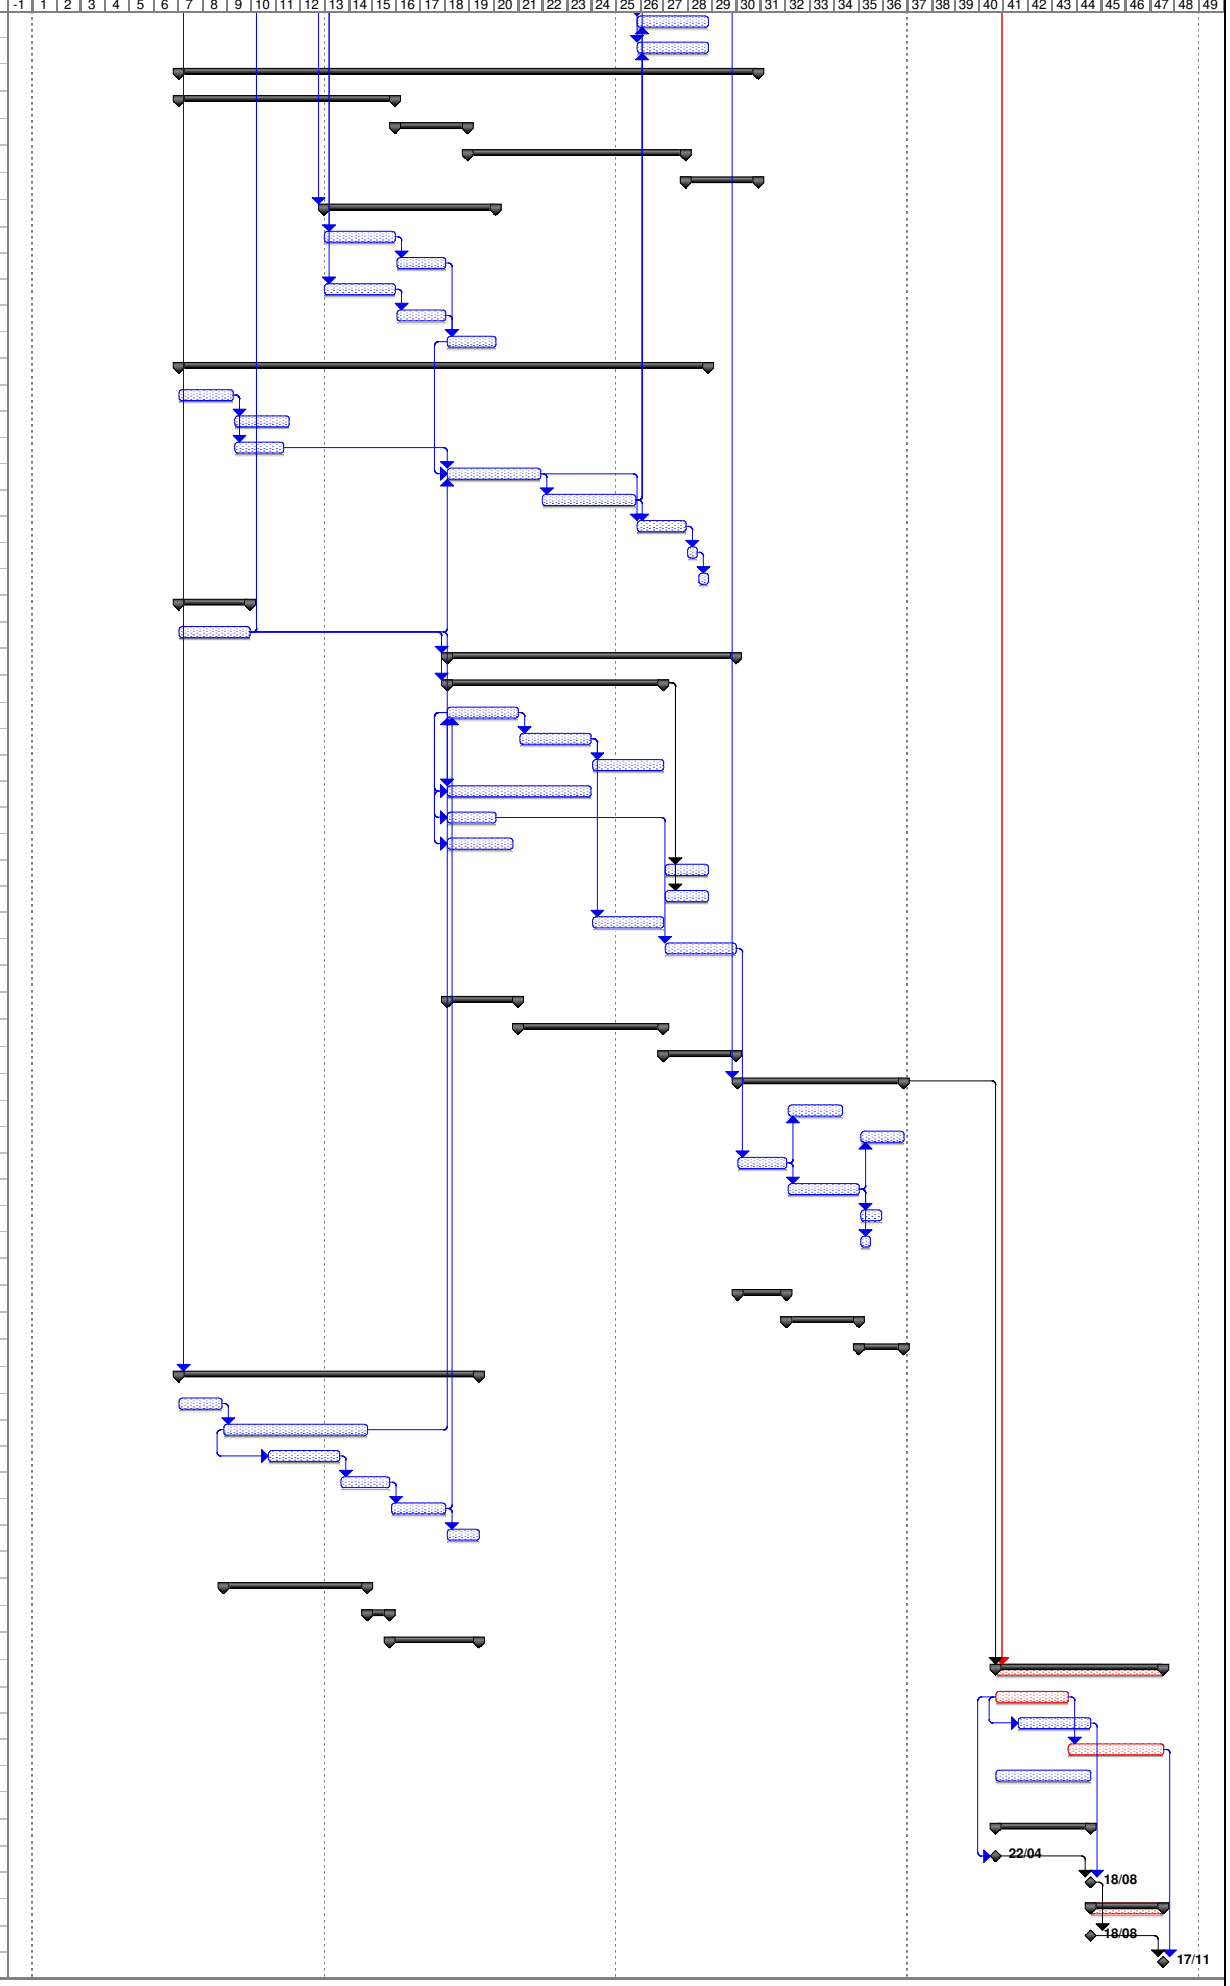

Project: Construction Prog 20111112_
Date: 14/11/11

Task Task Milestone Summary
